| ID | | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names |
|---|---|---|---|---|---|---|---|---|
| 1 | | | Underground Drainage | 10 days | Mon 17/05/21 | Fri 28/05/21 | | BJM |
| 2 | | | Building Works - Brick / Block | 45 days | Thu 01/04/21 | Wed 02/06/21 | | BJM |
| 3 | | | Ground Works - Structure | 50 days | Thu 01/04/21 | Wed 09/06/21 | | BJM |
| 4 | | | Carpentry | 50 days | Thu 01/04/21 | Wed 09/06/21 | | BJM |
| 5 | | | Glazing | 50 days | Thu 01/04/21 | Wed 09/06/21 | | BJM |
| 6 | | | Building Works - Dryline / Plastering | 50 days | Thu 01/04/21 | Wed 09/06/21 | | BJM |
| 7 | | | Ceilings - Suspended / Plaster Brd | 55 days | Thu 01/04/21 | Wed 16/06/21 | | CWC |
| 8 | | | Plumbing - Wet / Cold Services | 20 days | Mon 24/05/21 | Fri 18/06/21 | | Coxy |
| 9 | | | Plumbing - Heating | 60 days | Thu 01/04/21 | Wed 23/06/21 | | Coxy |
| 10 | | | Roofing | 40 days | Thu 01/04/21 | Wed 26/05/21 | | Gimson |
| 11 | | | Electrical - Data | 65 days | Thu 01/04/21 | Wed 30/06/21 | | Dorset Electrcial |
| 12 | | | Electrical - Lighting | 65 days | Thu 01/04/21 | Wed 30/06/21 | | Dorset Electrcial |
| 13 | | | Electrical - Power | 65 days | Thu 01/04/21 | Wed 30/06/21 | | Dorset Electrcial |
| 14 | | | Ground Works - Landscape | 30 days | Mon 24/05/21 | Fri 02/07/21 | | BJM |
| 15 | | | Fire Control | 30 days | Mon 24/05/21 | Fri 02/07/21 | | Dorset Fire & Security |
| 16 | | | Intruder Alarm | 30 days | Mon 24/05/21 | Fri 02/07/21 | | Dorset Fire & Security |
| 17 | | | Door Access Control | 30 days | Mon 24/05/21 | Fri 02/07/21 | | Dorset Fire & Security |
| 18 | | | Decoration | 55 days | Mon 03/05/21 | Fri 16/07/21 | | BJM |
| 19 | | | Joinery | 35 days | Mon 31/05/21 | Fri 16/07/21 | | BJM |
| 20 | | | Flooring | 40 days | Mon 24/05/21 | Fri 16/07/21 | | Prestiage |
| 21 | | | Site Clean - Removal of Compound | 2 days | Fri 16/07/21 | Mon 19/07/21 | | BJM |
| 22 | | | Hand-Over | 1 day | Wed 21/07/21 | Wed 21/07/21 | | BJM |
| 23 | | | Client Presence on site - Teachers moving in | 2 days | Mon 26/07/21 | Tue 27/07/21 | | Ambitions |

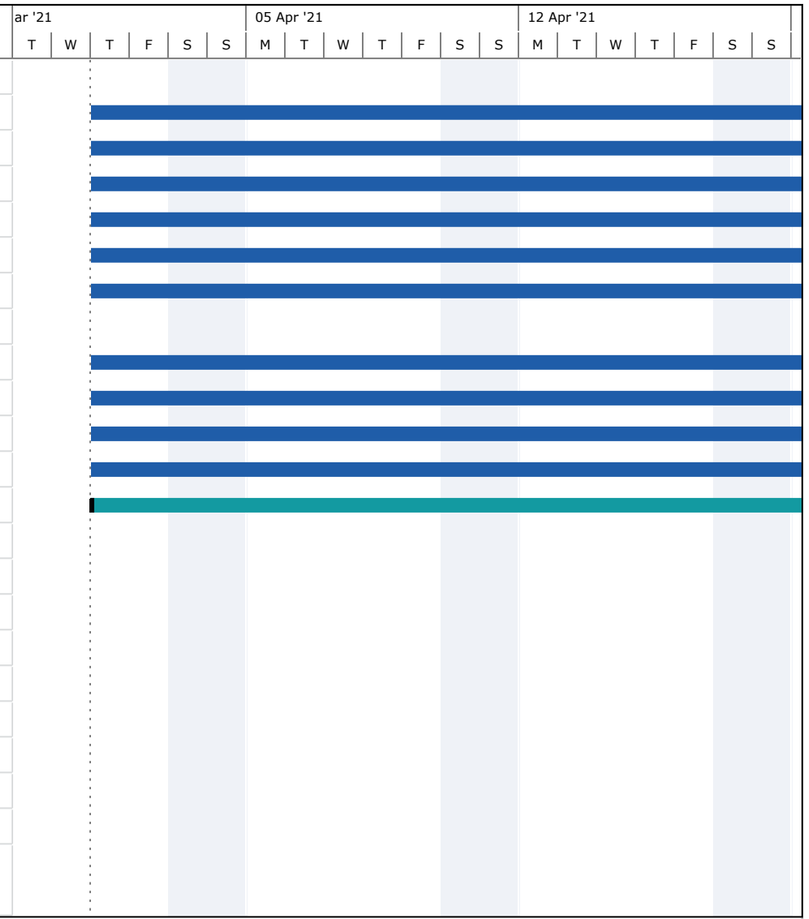

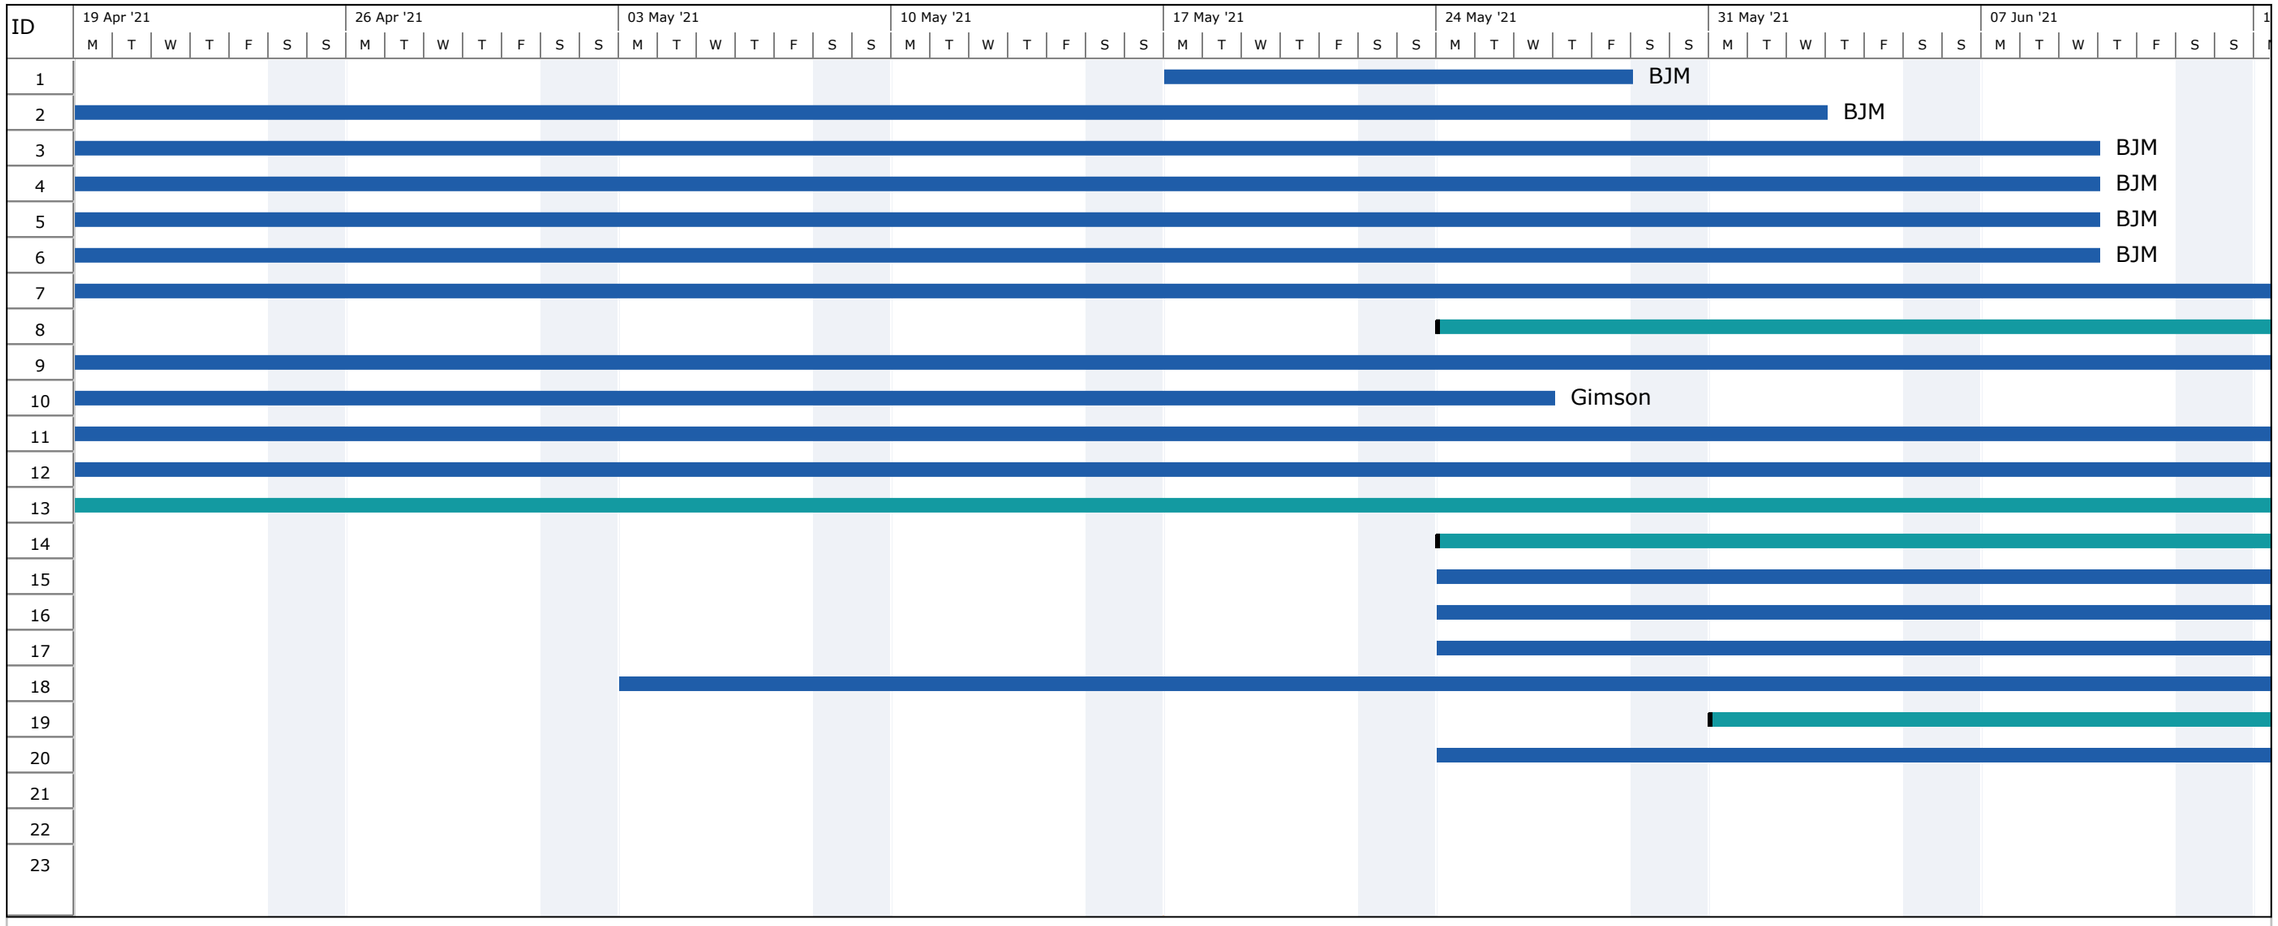
ID
19 Apr '21
26 Apr '21
03 May '21
10 May '21
17 May '21
24 May '21
31 May '21
07 Jun '21
M T W T F S S
1
2
3
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
BJM
BJM
BJM
BJM
BJM
BJM
Gimson

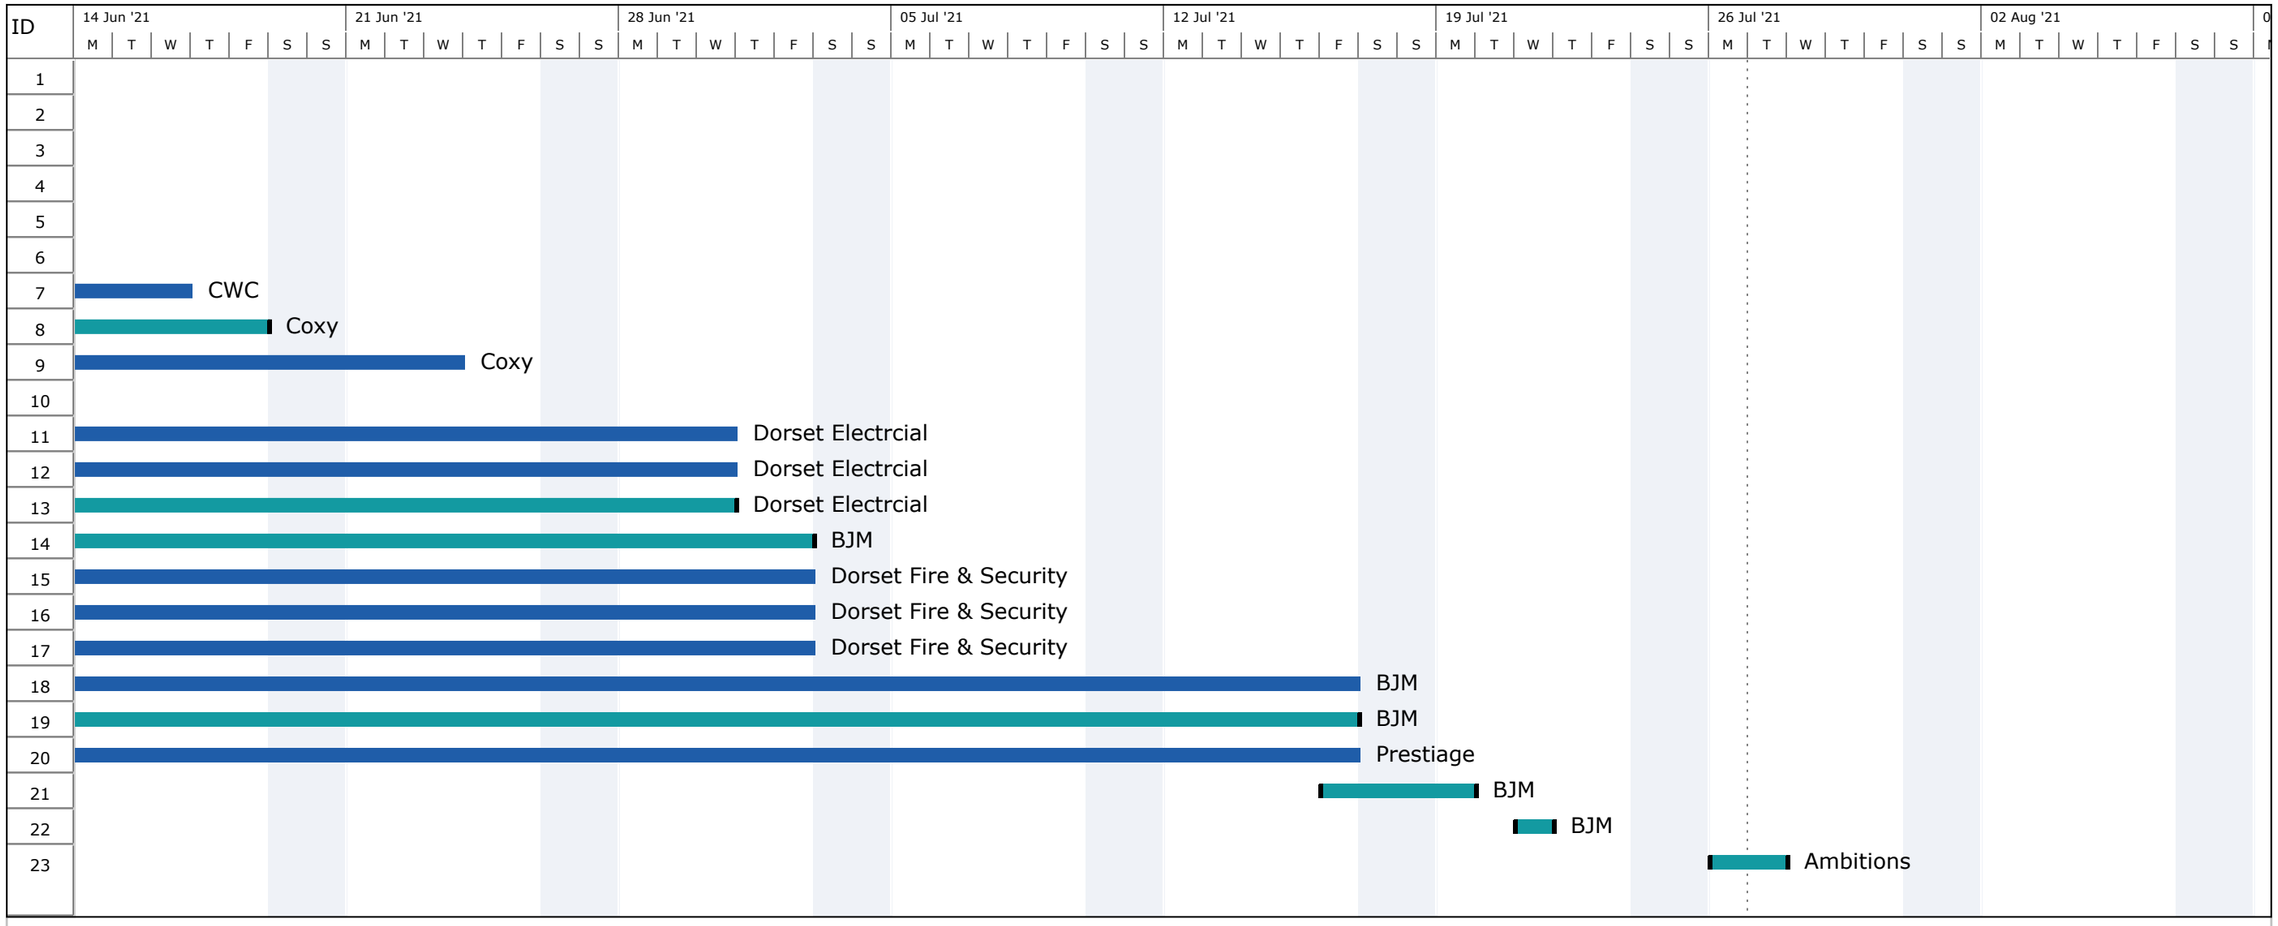
ID
14 Jun '21
21 Jun '21
28 Jun '21
05 Jul '21
12 Jul '21
19 Jul '21
26 Jul '21
02 Aug '21
M T W T F S S
1
2
3
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
CWC
Coxy
Coxy
Dorset Electrcial
Dorset Electrcial
Dorset Electrcial
BJM
Dorset Fire & Security
Dorset Fire & Security
Dorset Fire & Security
BJM
BJM
Prestiage
BJM
BJM
Ambitions
